



1250 West Century Avenue
Mailing Address:
P.O. Box 5601
Bismarck, ND 58506-5601
(701) 530-1600

May 1, 2024

Debbie-Anne Reese, Acting Secretary
Federal Energy Regulatory Commission
888 First Street, N.E., Room 1A
Washington, D.C. 20426

Re: WBI Energy Transmission, Inc.
Wahpeton Expansion Project
Docket No. CP22-466-000
Weekly Status Report No. 22

Dear Acting Secretary Reese:

WBI Energy Transmission, Inc. (WBI Energy) herewith submits its Weekly Status Report No. 22 for the Wahpeton Expansion Project, in compliance with Environmental Condition 9 of the Appendix to the Federal Energy Regulatory Commission's October 23, 2023 Order Issuing Certificate in the above referenced docket.

The attached report addresses the status of the project from April 22 to April 28, 2024.

Should you have any questions or comments regarding this filing, please call the undersigned at (701) 530-1563.

Sincerely,

/s/ Lori Myerchin

Lori Myerchin
Director, Regulatory Affairs and
Transportation Services

Attachment

cc: via email
David Hanobic, FERC Environmental Project Manager
Dawn Ramsey, FERC
Official Service List



WBI Energy Transmission, Inc.
Wahpeton Expansion Project
FERC Docket No. CP22-466-000
 Project Status Report No. 22
 Reporting Period: 4-22-2024 – 4-28-2024

A. Update on Federal Authorizations

- WBI Energy has obtained all necessary federal permits and authorizations required for construction of the Wahpeton Expansion Project.

B. Construction Status – Pipeline Facilities

- The Environmental Inspector provided onsite environmental training, as needed.
- Per WBI Energy’s response to Environmental Condition 7 to the Order Issuing Certificate, environmental training for WBI Energy and certain contract personnel will be held virtually on May 15, 2024. Environmental training for key contract personnel will be held in person on May 30, 2024 in Fargo, North Dakota.

TABLE 1-1 Wahpeton Expansion Pipeline ¹			
Work Completed during Reporting Period:			
<ul style="list-style-type: none"> • Continued receiving construction pipe at the 4 Suns contractor yard. 			
Activity	Total % Completed This Period	% of Total Job Completed	Comments
Pipeline			
Clearing / Grading	0%	<1%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Bores	0 of 72	0 of 72	
Cleanup	0%	0%	
Seeding	0%	0%	
Final Tie-in and Commissioning	0%	0%	
Hydrostatic Testing	0 of 1	0 of 1	
Appurtenant Facilities ²			
Block Valve #1 and Pig Launcher / Receiver #1 at MP 0.0	0 of 2	0 of 2	
Cleanup/Restoration	0%	0%	
Block Valve #2 and Pig Launcher / Receiver #2 at MP 11.6	0 of 2	0 of 2	
Cleanup/Restoration	0%	0%	
Block Valve #3 at MP 23.4	0 of 1	0 of 1	
Cleanup/Restoration	0%	0%	
Block Valve #4 at MP 31.3	0 of 1	0 of 1	
Cleanup/Restoration	0%	0%	


¹ The pipeline may be constructed as one or two spreads, pending the award of the pipeline contract. If two construction spreads are used, Table 1-1 will be modified accordingly.

² Cleanup/Restoration includes backfilling and spreading of gravel.



WBI Energy Transmission, Inc.
Wahpeton Expansion Project
FERC Docket No. CP22-466-000
 Project Status Report No. 22
 Reporting Period: 4-22-2024 – 4-28-2024

Block Valve #5 and Pig Launcher / Receiver #3 at MP 39.5	0 of 2	0 of 2		
Cleanup/Restoration	0%	0%		
Block Valve #6 at MP 48.9	0 of 1	0 of 1		
Cleanup/Restoration	0%	0%		
Block Valve #7 and Pig Launcher / Receiver #4 at MP 60.5	0 of 2	0 of 2		
Cleanup/Restoration	0%	0%		
Work Planned for next Reporting Period and Schedule Changes:				
<ul style="list-style-type: none"> Continue receiving construction pipe at the 4 Suns contractor yard. 				
Problem Areas, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> No problem areas were identified during reporting period. 				
Non-Compliance Issues, Corrective Actions and Effectiveness:				
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. 				
Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:				
<ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. 				
Copies included: Not applicable				
Landowner Issues: None				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

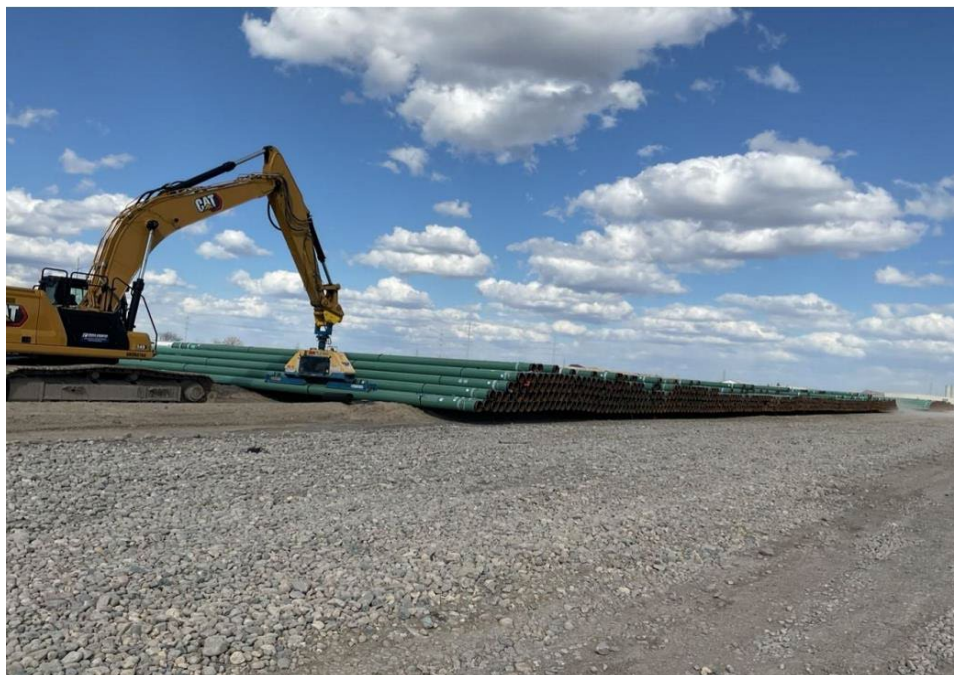

Date: 4/22/2024
 Location: 4 Suns Contractor Yard.
 Notes: Pipe unloading operations.



WBI Energy Transmission, Inc.
Wahpeton Expansion Project
FERC Docket No. CP22-466-000
Project Status Report No. 22
Reporting Period: 4-22-2024 – 4-28-2024



Date: 4/24/2024

Location: 4 Suns Contractor Yard.

Notes: Overview of contractor yard.



Date: 4/26/2024

Location: 4 Suns Contractor Yard.

Notes: Pipe unloading operations.



WBI Energy Transmission, Inc.
Wahpeton Expansion Project
FERC Docket No. CP22-466-000
 Project Status Report No. 22
 Reporting Period: 4-22-2024 – 4-28-2024

C. Construction Status – Aboveground Facilities

TABLE 2-1 Modifications at Mapleton Compressor Station				
Work Completed during Reporting Period: <ul style="list-style-type: none"> No work was completed during this reporting period. 				
Activity	Total % Completed This Period	% of Total Job Completed	Comments	
Install Aboveground Station Piping	0%	0%		
Install Belowground Station Piping	0%	0%		
Cleanup / Restoration ³	0%	0%		
Work Planned for next Reporting Period and Schedule Changes: <ul style="list-style-type: none"> No work is planned for the next reporting period. 				
Problem Areas, Corrective Actions and Effectiveness: <ul style="list-style-type: none"> No problem areas were identified during reporting period. 				
Non-Compliance Issues, Corrective Actions and Effectiveness: <ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. 				
Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses: <ul style="list-style-type: none"> No non-compliance issues were identified during reporting period. Copies included: Not applicable				
Landowner Issues: None				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

³ Final cleanup and restoration will be in conjunction with Block Valve #1 and Pig Launcher / Receiver #1 within the compressor station yard.



WBI Energy Transmission, Inc.
Wahpeton Expansion Project
FERC Docket No. CP22-466-000
 Project Status Report No. 22
 Reporting Period: 4-22-2024 – 4-28-2024

TABLE 2-2
MDU- Kindred Border Station

Work Completed during Reporting Period:

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Initial Site Work	0%	0%	
Concrete Work	0%	0%	
Install Aboveground Piping	0%	0%	
Install Belowground Piping	0%	0%	
Install Buildings	0%	0%	
Cleanup / Restoration ⁴	0%	0%	
Install Security Fence	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- No work is planned for the next reporting period.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues: None

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

⁴ Final cleanup and restoration will be completed in conjunction with Block Valve #3 within the border station yard.



WBI Energy Transmission, Inc.
Wahpeton Expansion Project
FERC Docket No. CP22-466-000
 Project Status Report No. 22
 Reporting Period: 4-22-2024 – 4-28-2024

TABLE 2-3
MDU- Wahpeton Border Station

Work Completed during Reporting Period:

- No work was completed during this reporting period.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
Initial Site Work	0%	0%	
Concrete Work	0%	0%	
Install Aboveground Piping	0%	0%	
Install Belowground Piping	0%	0%	
Install Buildings	0%	0%	
Cleanup / Restoration ⁵	0%	0%	
Install Security Fence	0%	0%	

Work Planned for next Reporting Period and Schedule Changes:

- No work is planned for the next reporting period.

Problem Areas, Corrective Actions and Effectiveness:

- No problem areas were identified during reporting period.

Non-Compliance Issues, Corrective Actions and Effectiveness:

- No non-compliance issues were identified during reporting period.

Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

Landowner Issues: None

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

⁵ Final cleanup and restoration will be completed in conjunction with Block Valve #7 and Pig Launcher / Receiver #4 within the border station yard.



WBI Energy Transmission, Inc.
Wahpeton Expansion Project
FERC Docket No. CP22-466-000
Project Status Report No. 22
Reporting Period: 4-22-2024 – 4-28-2024

D. Changes to Stream Crossings or Work in Environmental Sensitive Areas

TABLE 3
Changes to Stream Crossings or
Work in Environmental Sensitive Areas

Schedule changes to stream crossings.

- None during reporting period.

Schedule changes for work in other environmentally sensitive areas.

- None during reporting period.
