



---

1250 West Century Avenue  
Mailing Address:  
P.O. Box 5601  
Bismarck, ND 58506-5601  
(701) 530-1600

June 13, 2024

Debbie-Anne Reese, Acting Secretary  
Federal Energy Regulatory Commission  
888 First Street, N.E., Room 1A  
Washington, D.C. 20426

Re: WBI Energy Transmission, Inc.  
Wahpeton Expansion Project  
Docket No. CP22-466-000  
Weekly Status Report No. 28

Dear Acting Secretary Reese:

WBI Energy Transmission, Inc. (WBI Energy) herewith submits its Weekly Status Report No. 28 for the Wahpeton Expansion Project, in compliance with Environmental Condition 9 of the Appendix to the Federal Energy Regulatory Commission's October 23, 2023 Order Issuing Certificate in the above referenced docket.

The attached report addresses the status of the project from June 03, 2024 to June 09, 2024.

Should you have any questions or comments regarding this filing, please call the undersigned at (701) 530-1563.

Sincerely,

/s/ Lori Myerchin

Lori Myerchin  
Vice President, Regulatory Affairs  
and Transportation Services

Attachment

cc: via email  
David Hanobic, FERC Environmental Project Manager  
Dawn Ramsey, FERC  
Official Service List



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 28  
 Reporting Period: 6-03-2024 – 6-09-2024

**A. Update on Federal Authorizations**

- WBI Energy has obtained all necessary federal permits and authorizations required for construction of the Wahpeton Expansion Project.

**B. Construction Status – Pipeline Facilities**

- Environmental Inspectors held onsite environmental training for new contractor personnel on Tuesday, June 4, 2024, and continued to conduct onsite environmental training as needed.
- On June 11, 2024, FERC approved variance requests for project modifications submitted on June 4, 2024, as supplemented on June 10, 2024.

**TABLE 1-1**  
**Wahpeton Expansion Pipeline**

**Work Completed during Reporting Period:**

- Completed mobilization of construction equipment.
- Continued surveying and staking the construction right-of-way and approved access roads.
- Continued installation of Project signage.
- Continued staking existing drain tiles.
- Continued clearing/grading activities.
- Began installation of construction mats.
- Began installation of erosion control devices.
- Began installing goal posts at aboveground utility lines.

Activity	Total % Completed This Period	% of Total Job Completed	Comments
<b>Pipeline</b>			
Clearing / Grading	<1%	<1%	
Stringing	0%	0%	
Bending	0%	0%	
Welding	0%	0%	
Joint Coating	0%	0%	
Ditching	0%	0%	
Lowering	0%	0%	
Backfill	0%	0%	
Bores	0 of 70	0 of 70	
Cleanup	0%	0%	
Seeding	0%	0%	
Final Tie-in and Commissioning	0%	0%	
Hydrostatic Testing	0 of 1	0 of 1	
<b>Appurtenant Facilities <sup>1</sup></b>			
Valve Site #1 and Pig Launcher / Receiver #1 at MP 0.0	0 of 2	0 of 2	
Cleanup/Restoration	0%	0%	
Valve Site #2 and Pig Launcher / Receiver #2 at MP 11.6	0 of 2	0 of 2	
Cleanup/Restoration	0%	0%	
Valve Site #3 at MP 23.4	0 of 1	0 of 1	

<sup>1</sup> Cleanup/Restoration includes backfilling and spreading of gravel.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 28  
 Reporting Period: 6-03-2024 – 6-09-2024

Cleanup/Restoration	0%	0%	
Valve Site #4 at MP 31.3	0 of 1	0 of 1	
Cleanup/Restoration	0%	0%	
Valve Site #5 and Pig Launcher / Receiver #3 at MP 39.5	0 of 2	0 of 2	
Cleanup/Restoration	0%	0%	
Valve Site #6 at MP 48.9	0 of 1	0 of 1	
Cleanup/Restoration	0%	0%	
Valve Site #7 and Pig Launcher / Receiver #4 at MP 60.5	0 of 2	0 of 2	
Cleanup/Restoration	0%	0%	
<b>Work Planned for next Reporting Period and Schedule Changes:</b> <ul style="list-style-type: none"> <li>• Continue surveying and staking the construction right-of-way and approved access roads.</li> <li>• Continue installing and maintaining Project signage.</li> <li>• Continue installation of mats.</li> <li>• Continue installation of erosion control devices.</li> <li>• Continue installation of goal posts at aboveground utility lines.</li> <li>• Continue clearing/grading activities.</li> </ul>			
<b>Problem Areas, Corrective Actions and Effectiveness:</b> <ul style="list-style-type: none"> <li>• No problem areas were identified during reporting period.</li> </ul>			

**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 28  
 Reporting Period: 6-03-2024 – 6-09-2024

**Non-Compliance Issues, Corrective Actions and Effectiveness:**

Date	Milepost / Alignment Sheet #	Non-Compliance	Corrective Action
June 4, 2024	MP 0.66 / Sheet #1	Equipment off-ROW near access road AR-001.1 and Sta. No. 38+50. Two dozer operators simultaneously travelled approximately 15 to 17 feet outside of the clearly marked and staked ROW boundary for a distance of approximately 100 to 120 feet.	The Project was shut down and the EIs held a meeting with the construction crew stressing the importance of staying within the staked ROW. The staking plan was reviewed again with the construction crew. The landowner was informed of the off-ROW incident. The landowner will restore the area impacted by the off-ROW incident in conjunction with the future planting of the agricultural field.




Date: 6/06/2024

Location: Sta. No. 38+50.

Notes: Earth moving equipment off-ROW at approximately 38+50. Two dozer operators misinterpreted staking of approved workspace boundaries and travelled outside of approved workspace areas.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 28  
 Reporting Period: 6-03-2024 – 6-09-2024

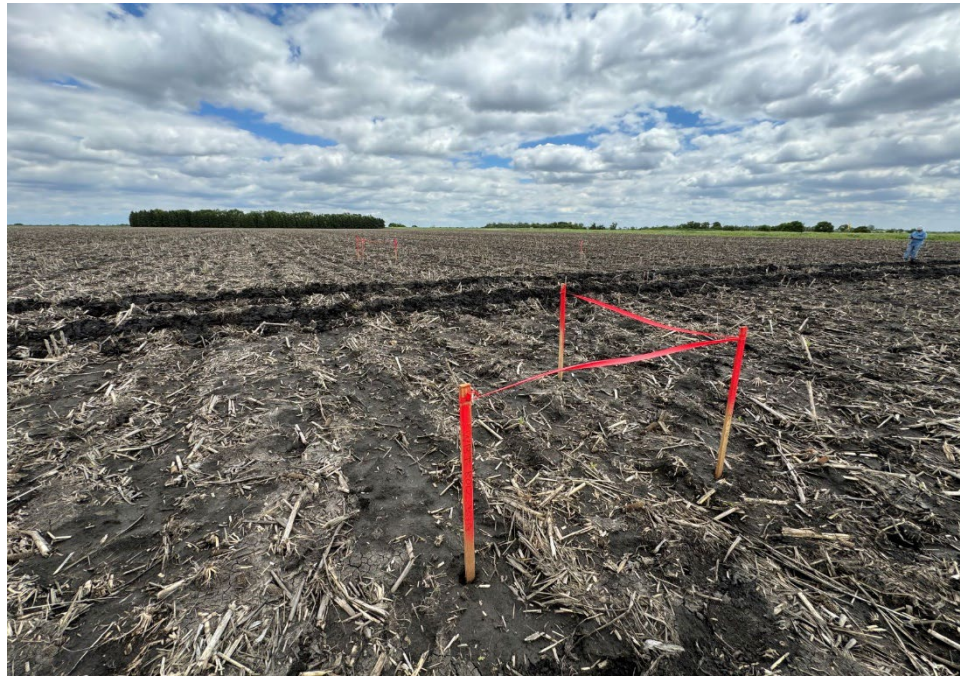

Date: 6/06/2024

Location: Sta. No. 38+50.

Notes: Earth moving equipment off-ROW at approximate Sta 38+50. Two dozer operators misinterpreted staking of approved workspace boundaries and travelled outside of approved workspace areas.

**Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:**

- No non-compliance issues were identified during reporting period.

Copies included: Not applicable

**Landowner Issues: None**

Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 28  
Reporting Period: 6-03-2024 – 6-09-2024



Date: 6/03/2024

Location: Sta. No. 903+00.

Notes: Installed signage for access road to construction right-of-way.



Date: 6/03/2024

Location: Sta. No. 1018+00.

Notes: Installed signage for access road to construction right-of-way.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 28  
Reporting Period: 6-03-2024 – 6-09-2024



Date: 6/05/2024

Location: Sta. No. 61+00.

Notes: Installed signage near Maple River along the construction right-of-way.



Date: 6/05/2024

Location: Sta. No. 195+00.

Notes: Looking west across construction right-of-way and access road. No Access and Pipeline Access Road signage has been installed.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 28  
Reporting Period: 6-03-2024 – 6-09-2024



Date: 6/05/2024

Location: Sta. No. 380+00.

Notes: Installed erosion control devices and goal posts along the construction right-of-way.



Date: 6/06/2024

Location: Sta. No. 40+00.

Notes: Installing mats along approved access road onto the construction right-of-way.





**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 28  
Reporting Period: 6-03-2024 – 6-09-2024



Date: 6/08/2024

Location: Sta. No. 240+00.

Notes: Installing heavy duty wattles on the construction right-of-way.



Date: 6/08/2024

Location: Sta. No. 260+00.

Notes: Installed signage at wetland wcaa002e on the construction right-of-way.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
Project Status Report No. 28  
Reporting Period: 6-03-2024 – 6-09-2024



Date: 6/08/2024

Location: Sta. No. 270+00.

Notes: Installed signage at wetland wcaa009e on the construction right-of-way.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 28  
 Reporting Period: 6-03-2024 – 6-09-2024

**C. Construction Status – Aboveground Facilities**

<b>TABLE 2-1</b> <b>Modifications at Mapleton Compressor Station</b>				
<b>Work Completed during Reporting Period:</b> <ul style="list-style-type: none"> <li>No work was completed during this reporting period.</li> </ul>				
Activity	Total % Completed This Period	% of Total Job Completed	Comments	
Install Aboveground Station Piping	0%	0%		
Install Belowground Station Piping	0%	0%		
Cleanup / Restoration <sup>2</sup>	0%	0%		
<b>Work Planned for next Reporting Period and Schedule Changes:</b> <ul style="list-style-type: none"> <li>No work is planned for the next reporting period.</li> </ul>				
<b>Problem Areas, Corrective Actions and Effectiveness:</b> <ul style="list-style-type: none"> <li>No problem areas were identified during reporting period.</li> </ul>				
<b>Non-Compliance Issues, Corrective Actions and Effectiveness:</b> <ul style="list-style-type: none"> <li>No non-compliance issues were identified during reporting period.</li> </ul>				
<b>Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:</b> <ul style="list-style-type: none"> <li>No non-compliance issues were identified during reporting period.</li> </ul> Copies included: Not applicable				
<b>Landowner Issues: None</b>				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

<sup>2</sup> Final cleanup and restoration will be in conjunction with Block Valve #1 and Pig Launcher / Receiver #1 within the compressor station yard.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 28  
 Reporting Period: 6-03-2024 – 6-09-2024

**TABLE 2-2**  
**MDU- Kindred Border Station**

<b>Work Completed during Reporting Period:</b>				
<ul style="list-style-type: none"> <li>No work was completed during this reporting period.</li> </ul>				
Activity	Total % Completed This Period	% of Total Job Completed	Comments	
Initial Site Work	0%	0%		
Concrete Work	0%	0%		
Install Aboveground Piping	0%	0%		
Install Belowground Piping	0%	0%		
Install Buildings	0%	0%		
Cleanup / Restoration <sup>3</sup>	0%	0%		
Install Security Fence	0%	0%		
<b>Work Planned for next Reporting Period and Schedule Changes:</b>				
<ul style="list-style-type: none"> <li>Survey and stake the border station workspace.</li> </ul>				
<b>Problem Areas, Corrective Actions and Effectiveness:</b>				
<ul style="list-style-type: none"> <li>No problem areas were identified during reporting period.</li> </ul>				
<b>Non-Compliance Issues, Corrective Actions and Effectiveness:</b>				
<ul style="list-style-type: none"> <li>No non-compliance issues were identified during reporting period.</li> </ul>				
<b>Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:</b>				
<ul style="list-style-type: none"> <li>No non-compliance issues were identified during reporting period.</li> </ul> Copies included: Not applicable				
<b>Landowner Issues: None</b>				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

<sup>3</sup> Final cleanup and restoration will be completed in conjunction with Block Valve #3 within the border station yard.



**WBI Energy Transmission, Inc.**  
**Wahpeton Expansion Project**  
**FERC Docket No. CP22-466-000**  
 Project Status Report No. 28  
 Reporting Period: 6-03-2024 – 6-09-2024

TABLE 2-3 MDU- Wahpeton Border Station				
<b>Work Completed during Reporting Period:</b>				
<ul style="list-style-type: none"> <li>No work was completed during this reporting period.</li> </ul>				
Activity	Total % Completed This Period	% of Total Job Completed	Comments	
Initial Site Work	0%	0%		
Concrete Work	0%	0%		
Install Aboveground Piping	0%	0%		
Install Belowground Piping	0%	0%		
Install Buildings	0%	0%		
Cleanup / Restoration <sup>4</sup>	0%	0%		
Install Security Fence	0%	0%		
<b>Work Planned for next Reporting Period and Schedule Changes:</b>				
<ul style="list-style-type: none"> <li>No work is planned for the next reporting period.</li> </ul>				
<b>Problem Areas, Corrective Actions and Effectiveness:</b>				
<ul style="list-style-type: none"> <li>No problem areas were identified during reporting period.</li> </ul>				
<b>Non-Compliance Issues, Corrective Actions and Effectiveness:</b>				
<ul style="list-style-type: none"> <li>No non-compliance issues were identified during reporting period.</li> </ul>				
<b>Non-Compliance Issues from Federal, State or Local Permitting Agencies and Responses:</b>				
<ul style="list-style-type: none"> <li>No non-compliance issues were identified during reporting period.</li> </ul> Copies included: Not applicable				
<b>Landowner Issues: None</b>				
Date	Name	Milepost / Alignment Sheet #	Problem/Concern	Corrective Action

**D. Changes to Stream Crossings or Work in Environmental Sensitive Areas**

TABLE 3 Changes to Stream Crossings or Work in Environmental Sensitive Areas
<b>Schedule changes to stream crossings.</b>
<ul style="list-style-type: none"> <li>None during reporting period.</li> </ul>
<b>Schedule changes for work in other environmentally sensitive areas.</b>
<ul style="list-style-type: none"> <li>None during reporting period.</li> </ul>

<sup>4</sup> Final cleanup and restoration will be completed in conjunction with Block Valve #7 and Pig Launcher / Receiver #4 within the border station yard.
